



May 2023



Progress

Sallins

Soil Nail System complete in Sallins. Geomesh layer and Hydroseeding installed to slope.

Timber Post and Rail Fence installed in Sallins alongside Church Avenue.

North and South Bridge Abutment constructed.

Works to soil steepened slopes to ramps commenced.

Unbound Towpath Works

Capping Layer 90% Complete. Sub Base and Quarry Dust to be placed start June.

Shared Surface/Bound Surface Works

Double Surface Dressing and section of Bound Surface at Sallins to follow late June.

General

Masonry Works at Underbridges complete

Programme


Works still on programme to be complete in October 2023, with the bridge to be installed for September and school reopening.



JOHN CRADOCK LTD



Soil Nailing/Hydroseeding along Church Rd

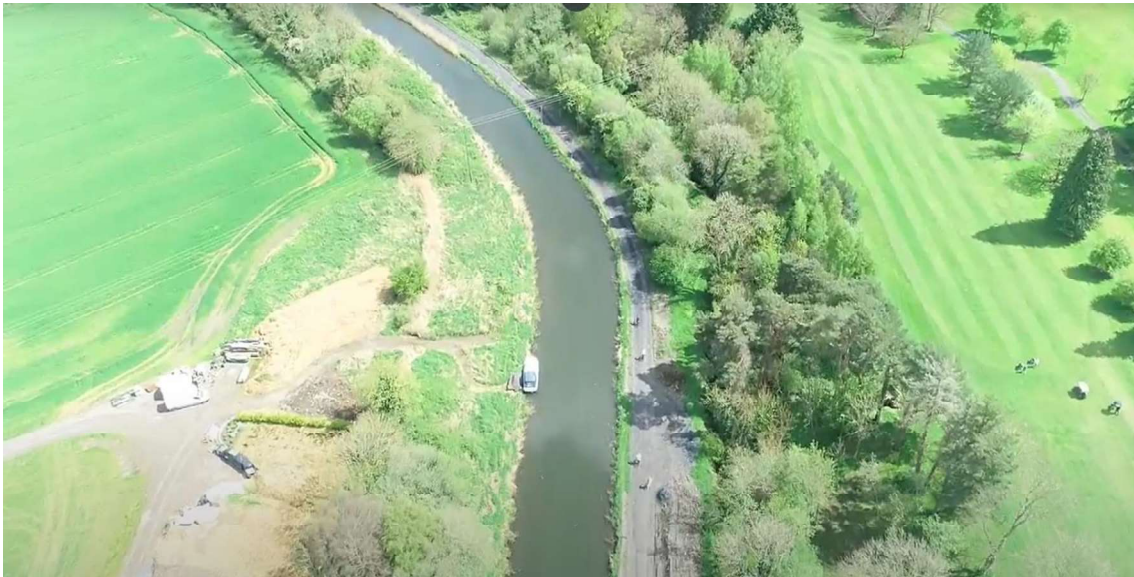

New Greenway Complete to Capping along Golf Course. Note active cyclists on Greenway



JOHN CRADOCK LTD



Works at Lock 15



Underbridge Access Reopened at Devonshire



JOHN CRADOCK LTD




Greenway Complete to Capping between Devonshire & Ponsonby



Access Reopened Under Ponsonby



Access Reopened under Henry Bridge

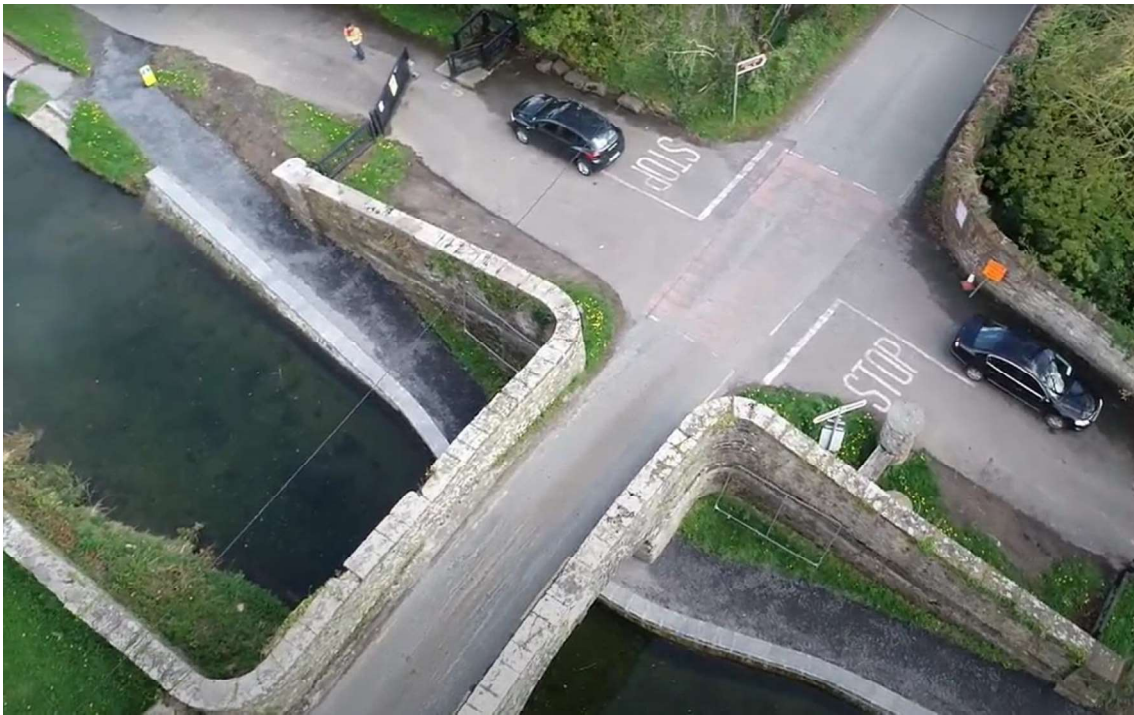

Access Reopened under Aylmer Complete
