

**Update March 2024**

**M7 Underpass towpath works ongoing, Works to be complete end March**





**Rathangan – 2 separate locations Works complete mid April.**


Spencer Bridge Location







Rathangan Bridge

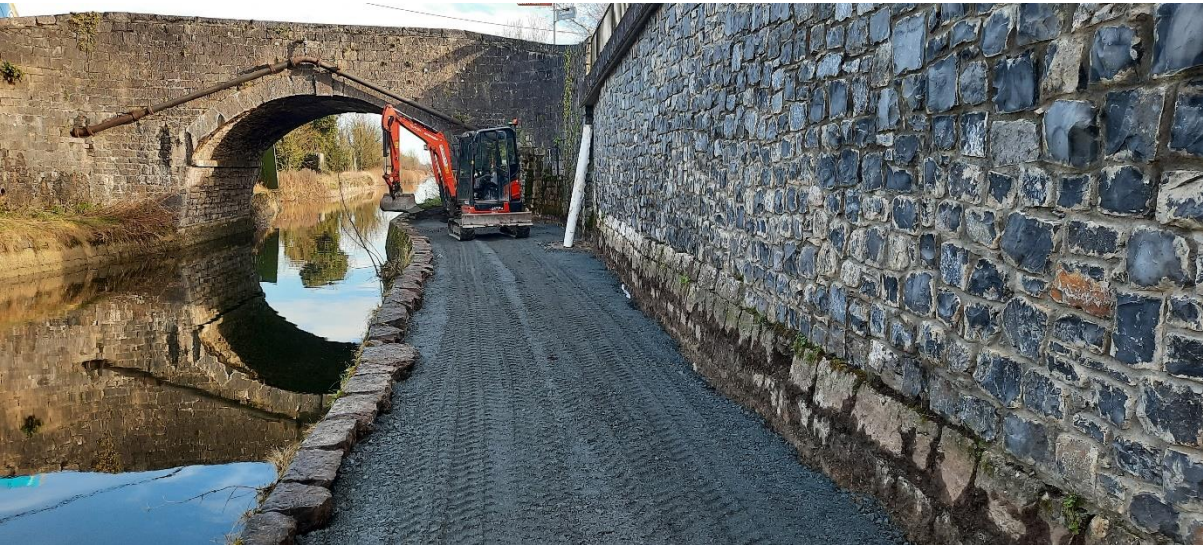





**Ummeras Bridge** – Works complete end of March





Clogheen Bridge – Works Complete end March







## **Works to Commence**

Augustus Bridge Athy – April 2024

Ballyteigue Area March 19<sup>th</sup> 2024

Herberton Bridge – April 2024.

Snagging will commence in April 2024

Additional Funding Application to RRDF Call 5 submitted for construction of the new pedestrian bridge in Rathangan and for Interpretive elements.
